




US Army Corps
of Engineers
Wilmington District

NAD/SAD/MVD/SWD REGIONAL DREDGING MEETING/WEDA

WILMINGTON DISTRICT FY 09 DREDGING PROGRAM


Wilmington District Dredging Schedule					Updated OCT 2008				
South Atlantic Division									
Project	Dredge Type	Estimated Quantity (Cubic Yards)	Disposal Area	FY09	FY10	FY11	FY12	FY13	
Operations & Maintenance (O&M) Projects:									
Wilmington Harbor Project (O&M):									
Anchorage Basin Contract	Pipeline	1,300,000	Eagle Island	X	X	X	X	X	
Outer Ocean Bar Contract	Hopper	850,000	Ocean	X	X	X	X	X	
Inner Ocean Bar Contract	Pipeline	1,000,000	Beach	X		X		X	
Mid-River Contract	Mechanical / Hopper	600,000	Ocean		X		X		
Morehead City Harbor Project (O&M):									
Ocean Bar Contract	Hopper	800,000	Nearshore	X	X	X	X	X	
Inner Harbor Contract	Mechanical / Pipeline	400,000	Ocean/Upland		X	X	X		
AIWV, NC Project (O&M):									
Dredging	Pipeline	500,000	Beach/Upland	X	X	X	X	X	
Dike Repairs				X	X	X	X	X	
Manteo (Shallowbag) Bay, NC Project (O&M):									
Interior Channel Contract	Pipeline	600,000	Upland/Bird Island	X	X	X	X	X	
Spit Contract	Pipeline	500,000	Beach			X			
Ocean Bar Contract	Hopper	300,000	Nearshore		X		X		
Beach Renourishment Projects (CG):									
Wrightsville Beach / Masonboro Island	Pipeline	900,000	Beach		X				
Carolina Beach	Pipeline	500,000	Beach		X			X	
Kure Beach	Pipeline	350,000	Beach		X			X	
Ocean Isle Beach	Pipeline	500,000	Beach		X			X	
Support For Others Projects:									
Military Ocean Terminal Sunny Point (MOTS)	Mechanical	1,500,000	Ocean	X	X	X	X	X	

Note: Scheduled Projects Subject to Receiving Federal Funds

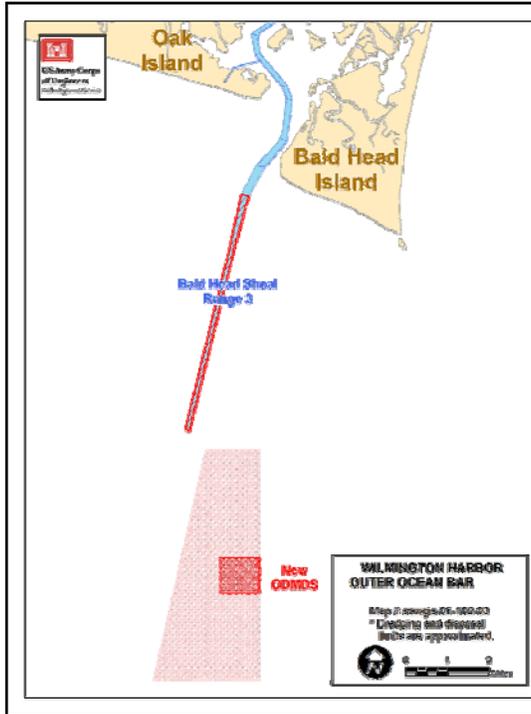



PROJECT: Wilmington Harbor Ocean Bar


TYPE WORK: Maintenance
DEPTH: 44 + 2
WIDTH: 500 ft – 900 ft
LENGTH: 3.45 Miles
QUANTITY: 750,000 cy
TYPE OF MATERIAL: Silt
PLACEMENT AREA: Offshore Disposal
DISTANCE TO PLACEMENT AREA: 5 – 8 miles
TYPE OF EQUIPMENT: Hopper
SMALL BUSINESS SET ASIDE: No
LAST DREDGED: March 2008
ENVIRONMENTAL WINDOW: Dec. 1 – Mar. 31
REASON FOR WINDOW: Sea Turtles
START DATE: January 1, 2009
CONTRACT COMPLETION DATE: March 31, 2009
FY 09 FUNDING: Yes

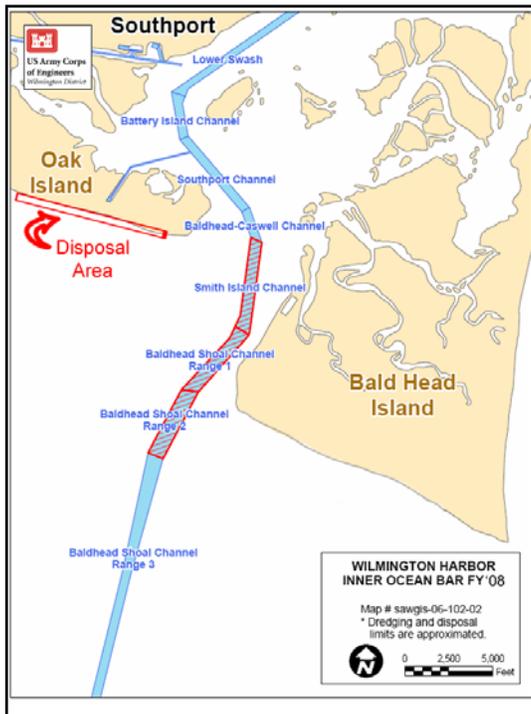


PROJECT: Wilmington Harbor Ocean Bar

TYPE WORK: Maintenance
DEPTH: 44' + 2
WIDTH: 650 ft – 900 ft
LENGTH: Varies
QUANTITY: 1,000,000 cy
TYPE OF MATERIAL: Silt
PLACEMENT AREA: Oak Island
DISTANCE TO PLACEMENT AREA: Varies
TYPE OF EQUIPMENT: Pipeline/Hopper Pump Out
SMALL BUSINESS SET ASIDE: No
LAST DREDGED: April 2007
ENVIRONMENTAL WINDOW: Nov. 16 – April 30 (Beach)
 Dec. 1 – March 31 (Hopper)
START DATE: January 1, 2009
CONTRACT COMPLETION DATE: March 31, 2009 (Hopper)
 April 30, 2009 (Beach)
FY 09 FUNDING: Yes

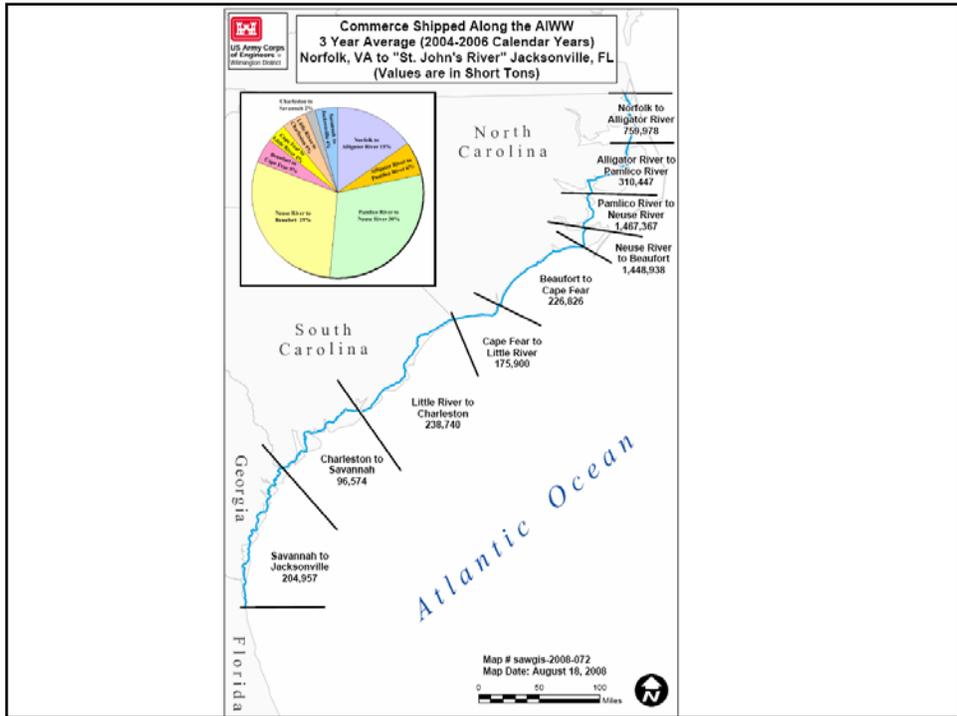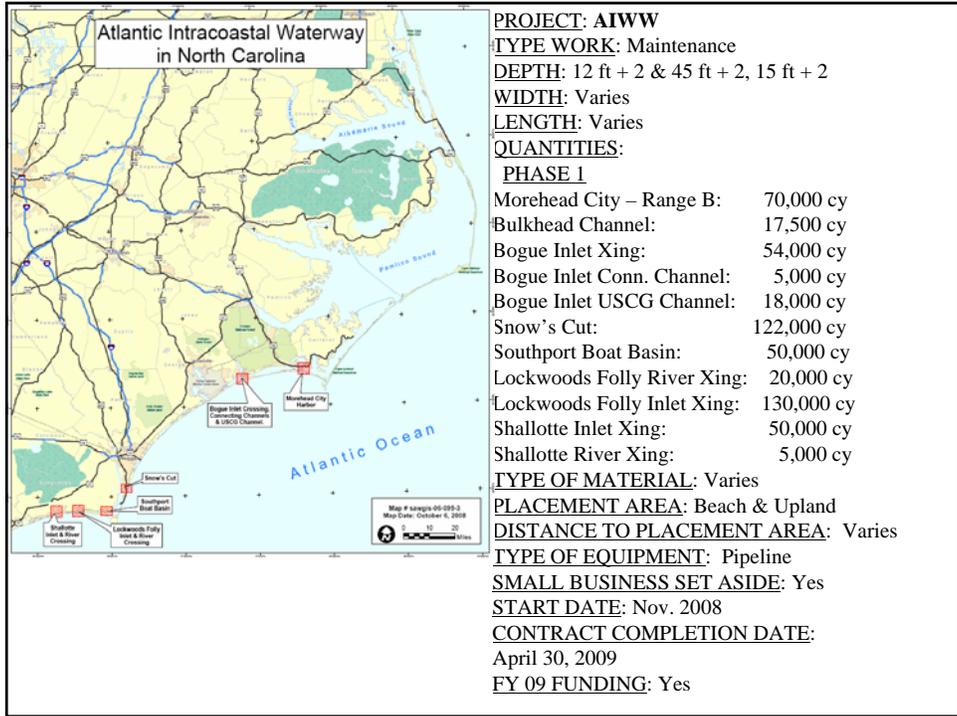


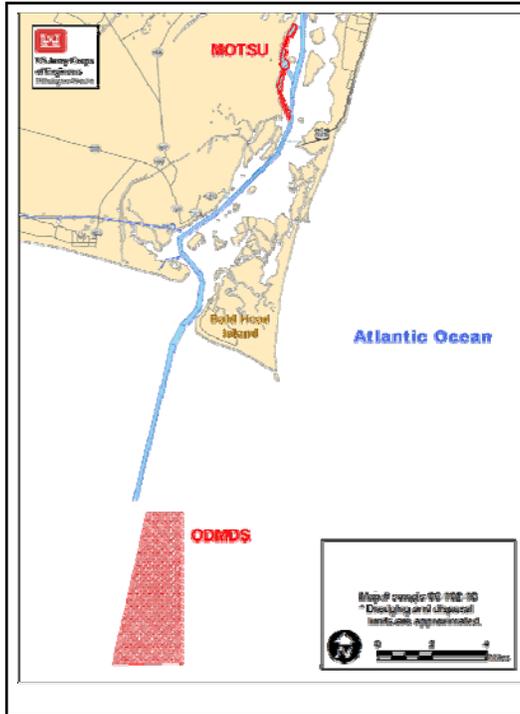


PROJECT: MOTSU
TYPE WORK: Maintenance
DEPTH: 38'+2 & 34'+2
WIDTH: Varies
LENGTH: Entrance Channel and Basins
QUANTITY: 920,000 cy
TYPE OF MATERIAL: Silt
PLACEMENT AREA: New ODMDS
DISTANCE TO PLACEMENT AREA:
 Approximately 20 miles
TYPE OF EQUIPMENT: Bucket & Barge
SMALL BUSINESS SET ASIDE: No
LAST DREDGED: Annually
ENVIRONMENTAL WINDOW: None
REASON FOR WINDOW: N/A
START DATE: Nov 2008
CONTRACT COMPLETION DATE:
 Jan. 2009
FY 09 FUNDING: Yes

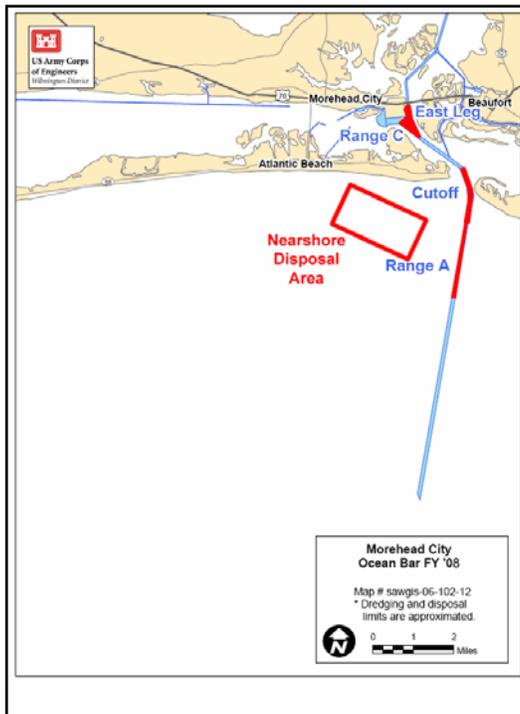

PROJECT: Morehead City Ocean Bar
TYPE WORK: Maintenance
DEPTH: 45 + 2
WIDTH: 600-650 ft
LENGTH: ~ 2.5 miles
QUANTITY: 550,000 cy
TYPE OF MATERIAL: Sand
PLACEMENT AREA: Nearshore
DISTANCE TO PLACEMENT AREA:
 Varies
TYPE OF EQUIPMENT:
 Govt. Hopper McFarland
SMALL BUSINESS SET ASIDE: No
LAST DREDGED: March 2008
ENVIRONMENTAL WINDOW:
 Jan 1 – March 31
REASON FOR WINDOW: Sea Turtles
START DATE: Jan 2009
CONTRACT COMPLETION DATE:
 March 2009
FY 09 FUNDING: Yes

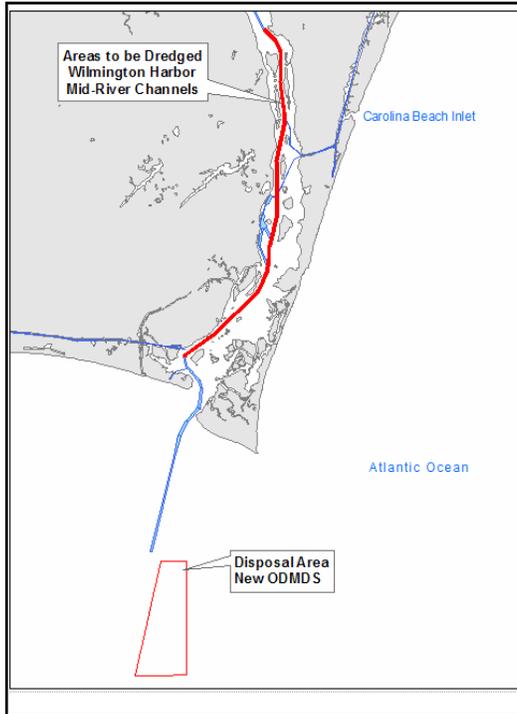

PROJECT: Wilmington Harbor Mid-River
TYPE WORK: Maintenance
DEPTH: 42' + 2'
WIDTH: Varies
LENGTH: Varies
QUANTITY: 500,000 cy
TYPE OF MATERIAL: Silt
PLACEMENT AREA: New ODMDS
DISTANCE TO PLACEMENT AREA: Approximately 20 Miles
TYPE OF EQUIPMENT: Hopper
SMALL BUSINESS SET ASIDE: No
ENVIRONMENTAL WINDOW: Dec. 1 – March 31 (Hopper Only)
 FY09 – FY2010 Combined with Wilmington Harbor Ocean Bar Channel Dredging.

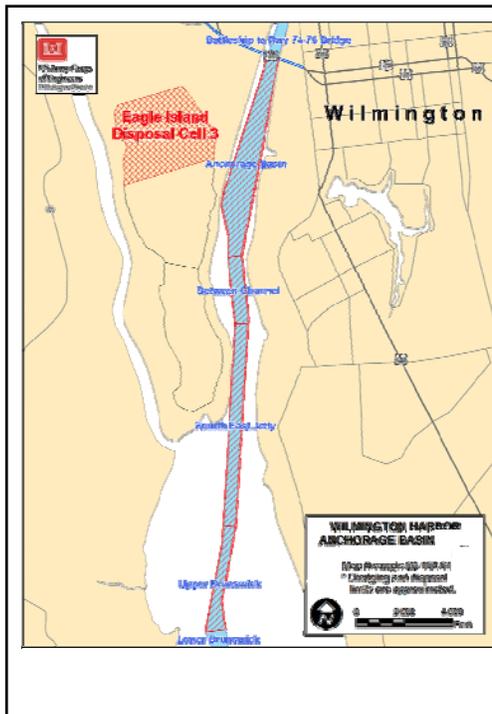

PROJECT: Wilmington Harbor, Anchorage Basin
TYPE WORK: Maintenance Dredging
DEPTH: 38'+2 & 42'+2
WIDTH: Varies
LENGTH: Varies
QUANTITY: 1,390,000
TYPE OF MATERIAL: Silt
PLACEMENT AREA: Eagle Island, Cell 3
DISTANCE TO PLACEMENT AREA: Varies
TYPE OF EQUIPMENT: Pipeline
SMALL BUSINESS SET ASIDE: Yes
LAST DREDGED: 2007
ENVIRONMENTAL WINDOW: Aug. 1 – Jan. 31
START DATE: Sept 23, 2008
COMPLETION DATE: January 2009
FY 09 FUNDING: Yes
CONTRACTOR: Southern Dredging

Wilmington District Points of Contact

Navigation Branch Chief: Mr. Roger Bullock
(910) 251-4822
Roger.D.Bullock@usace.army.mil

Waterways Management Section: Mr. Jimmy Hargrove
(910) 251-4479
James.T.Hargrove@usace.army.mil

Navigation Contract Questions: Mr. Danny Kissam
(910) 251-4424
Danny.R.Kissam@usace.army.mil

Current Construction Contracts: Mr. Jim Mullins
(910) 251-4816
James.M.Mullins@usace.army.mil
